

# ROOSEVELT

## CONSTRUCTION NEWSLETTER

LEASE CRUTCHER  
**Lewis**

October 2015

Portland Public Schools, Roosevelt High School Modernization Project

### PROJECT TEAM CONTACTS

**Nate Buddress: Project Manager**

971.563.0020 | [nate.buddress@lewisbuilds.com](mailto:nate.buddress@lewisbuilds.com)

**Chad Nielson: Superintendent**

503.572.0135 | [chad.nielson@lewisbuilds.com](mailto:chad.nielson@lewisbuilds.com)

### UPCOMING MILESTONES

- Existing Auditorium interior demolition complete: October 2nd
- New Orchestra Pit at Performing Arts footings complete: October 7th
- New Gym CMU installation begins: October 15th
- New Gym slab on grade pour complete: October 22nd
- New Performing Arts stairs poured: October 23rd
- New Media Center and Library ground level shear walls and footings in process: throughout October

The existing auditorium demolition is nearly complete. Following this demolition Lewis will construct new shearwalls in the basement for the New Media Center and Library.

The New Gym footings are nearly complete. CMU walls will start in earnest and the New Gym slab on grade will be poured towards the end of this month. The New Performing Arts mass grading is under construction and the new Orchestra Pit will be complete by the 2nd week of October.


Underground mechanical, electrical, plumbing, and fire protection for the new Performing Arts are progressing this month. New stairs in the Performing Arts building will also be poured towards the end of the month. There is much activity and excitement taking place as we begin construction of the new buildings.

Sincerely,




Michael C. Kingham

Senior Project Engineer, Roosevelt High School Modernization Project

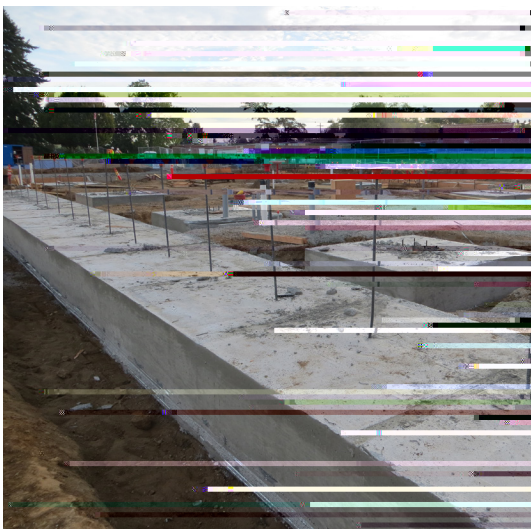

# ROOSEVELT MODERNIZATION

October 2015

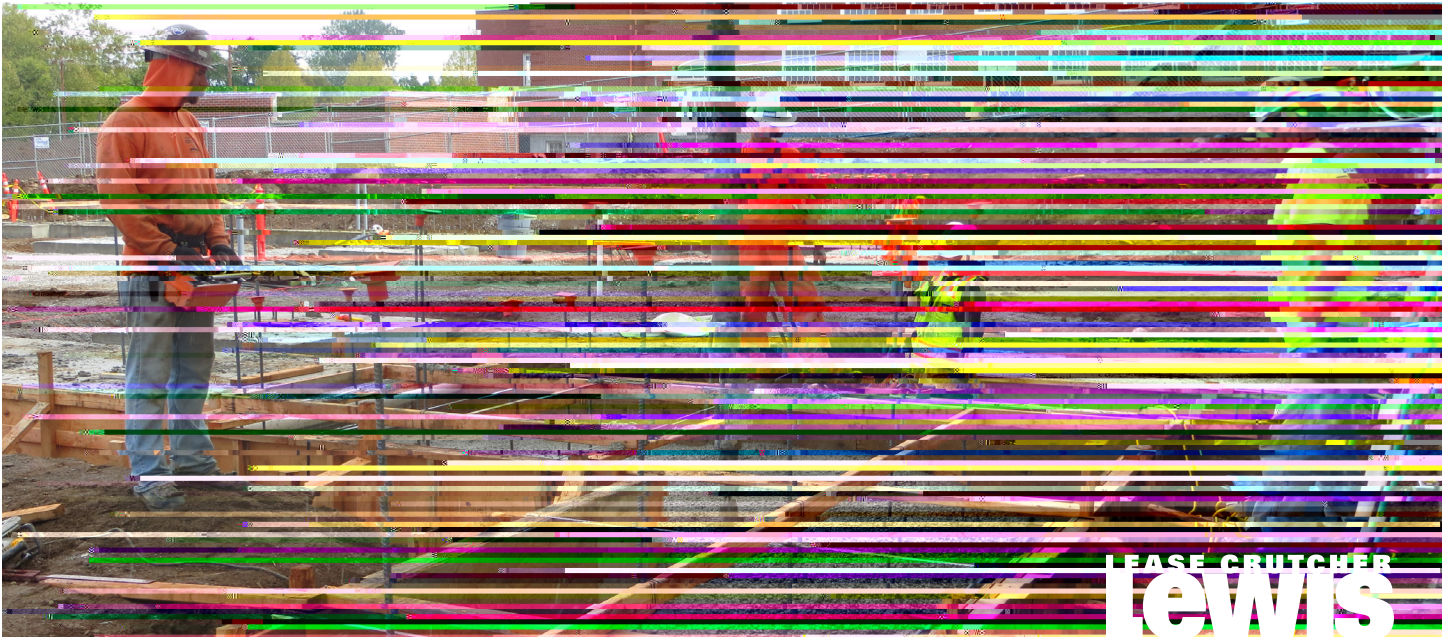

LEASE CRUTCHER  
**lewis**
